

Field Impact Sound Transmission Test Report

Apparent Impact Insulation Class (AIIc)

Report Date:	April 18, 2024	Source Room:	2nd Floor Bed 1, Volume: 1176 cu. ft.
Test Date:	April 04, 2024	Receiver Room:	1st Floor Bed 1, Volume: 1413 cu. ft.
DLAA Test No:	1.4.1	Test Assembly:	Floor-ceiling, Area: 130 sq. ft.

Test Site:	Ka'ulu by Gentry
Client:	Gentry Builders, LLC

STANDARDS

ASTM E1007-14	Standard Test Method for Field Measurement of Tapping Machine Impact Sound Transmission Through Floor-Ceiling Assemblies and Associated Support Structure
ASTM E989-06(2012)	Standard Classification for Determination of Impact Insulation Class (IIC)
ASTM E2235-04(2012)	Standard Test Method for Determination of Decay Rates for Use in Sound Insulation Test Methods

STATEMENT OF CONFORMANCE:

Testing was conducted in general accordance with ASTM E1007-14, with all exceptions noted below. All requirements for measuring and reporting Absorption Normalized Impact Sound Pressure Level (ANISPL) and Apparent Impact Insulation Class (AIIc) were met.

TEST ENVIRONMENT:

The source room was 2nd Floor Bed 1. The space was finished, unfurnished. The floor was Carpet. The ceiling was gyp. The walls were gyp. All doors and windows were closed during the testing period. The source room had a volume of approximately 1176 cu. ft.

The receiver room was 1st Floor Bed 1. The space was finished, unfurnished. The floor was LVT. The ceiling was gyp. The walls were gyp. All doors and windows were closed during the testing period. The receiver room had a volume of approximately 1413 cu. ft.

The test assembly measured approximately 12.3x10.6, and had an approximate area of 130 sq. ft.

TEST ASSEMBLY:

The tested assembly was the Floor-ceiling. The assembly was not field verified, and was based on information provided by the client and drawings for the project. The client advised that no slab treatment or self-leveling was applied. Results may vary if slab treatment or self-leveling or any adhesive is used in other installations.

Field Impact Sound Transmission Test Report

Apparent Impact Insulation Class (AIIc)

Report Date:	April 18, 2024	Source Room:	2nd Floor Bed 1, Volume: 1176 cu. ft.
Test Date:	April 04, 2024	Receiver Room:	1st Floor Bed 1, Volume: 1413 cu. ft.
DLAA Test No:	1.4.1	Test Assembly:	Floor-ceiling, Area: 130 sq. ft.
Test Site:	Ka'ulu by Gentry		
Client:	Gentry Builders, LLC		

TEST PROCEDURE:

The test was performed in general accordance with ASTM E1007-14. Determination of Space-Average Levels performed via the manually scanned microphones technique, described in ASTM E1007-14, Paragraph 11.4.2.2.

Flanking transmission was not evaluated.

To evaluate room absorption, 1 microphone was used to measure 4 decays at 4 locations around the receiving room for a total of 16 measurements, per ASTM E2235-04(2012).

TEST INSTRUMENTATION:

Equipment Type	Manufacturer	Model Number	Serial Number	Last NIST Traceable Calibration	Last Local Calibration
Tapping Machine:	Norsonics	CAL200	2775671	9/19/2022	N/A
Sound Level Meter	Larson Davis	831	4328	10/24/2022	4/4/2024
Microphone Pre-Amp	Larson Davis	PRM831	046469	10/24/2022	4/4/2024
Microphone	Larson Davis	377B20	168830	10/20/2022	4/4/2024
Calibrator	Larson Davis	CAL200	5955	10/26/2022	N/A
Amplified Loudspeaker	QSC	K10	GAA530909	N/A	N/A
Noise Generator	NTi Audio	MR-PRO	0162	N/A	N/A

Field Impact Sound Transmission Test Report

Apparent Impact Insulation Class (AIIC)

Report Date:	April 18, 2024	Source Room:	2nd Floor Bed 1, Volume: 1176 cu. ft.
Test Date:	April 04, 2024	Receiver Room:	1st Floor Bed 1, Volume: 1413 cu. ft.
DLAA Test No:	1.4.1	Test Assembly:	Floor-ceiling, Area: 130 sq. ft.
Test Site:	Ka'ulu by Gentry		
Client:	Gentry Builders, LLC		

STATEMENT OF TEST RESULTS:

Frequency	Absorption Normalized Impact Sound Pressure Level, ANISPL (dB)	Average Receiver Background Level	Average RT60 (Seconds)	Exceptions noted to ASTM E1007-14	
100 Hz	57.0	39.7	0.73		
125 Hz	49.0	38.6	0.66		
160 Hz	47.0	34.0	0.57		
200 Hz	41.0	38.4	0.86		
250 Hz	39.0	34.2	1.59		2
315 Hz	44.0	25.8	1.17		
400 Hz	38.0	23.5	1.32		2
500 Hz	32.0	23.8	1.47		2
630 Hz	26.0	21.1	1.34		2
800 Hz	23.0	19.2	1.22		2
1000 Hz	18.0	19.3	1.35	1	2
1250 Hz	17.0	16.5	1.50		2
1600 Hz	16.0	14.7	1.64		2
2000 Hz	16.0	11.9	1.57		2
2500 Hz	16.0	10.2	1.46		
3150 Hz	14.0	9.4	1.26		
4000 Hz	10.0	11.9	1.33		
5000 Hz	9.0	10.6	1.36		

*This test does not fully conform to the requirements of ASTM E1007-13, so the calculated AIIC rating should be considered a minimum.

Notes:

1. The signal-to-noise ratio is less < 5 dB at this frequency band.
2. Airborne sound flanking is within 10 dB of impact sound pressure measurements at this frequency band.

AIIC: 63

An Apparent Impact Insulation Class (AIIC) of 63 and an Impact Sound Rating (ISR) of 70 was calculated. The AIIC rating is based on Absorption Normalized Impact Sound Pressure Level (ANISPL), and includes the effects of noise flanking. The AIIC reference contour is shown on the next page, and has been "fit" to the ANISPL values, in accordance with the procedure of ASTM E989-06(2012).

The results stated in this report represent only the specific construction and acoustical conditions present at the time of the test. Measurements performed in accordance with this test method on nominally identical constructions and acoustical conditions may produce different results.


Field Impact Sound Transmission Test Report

Apparent Impact Insulation Class (AIIC)

Report Date: April 18, 2024
Test Date: April 04, 2024
DLAA Test No: 1.4.1

Source Room: 2nd Floor Bed 1, Volume: 1176 cu. ft.
Receiver Room: 1st Floor Bed 1, Volume: 1413 cu. ft.
Test Assembly: Floor-ceiling, Area: 130 sq. ft.

Test Site: Ka'ulu by Gentry
Client: Gentry Builders, LLC

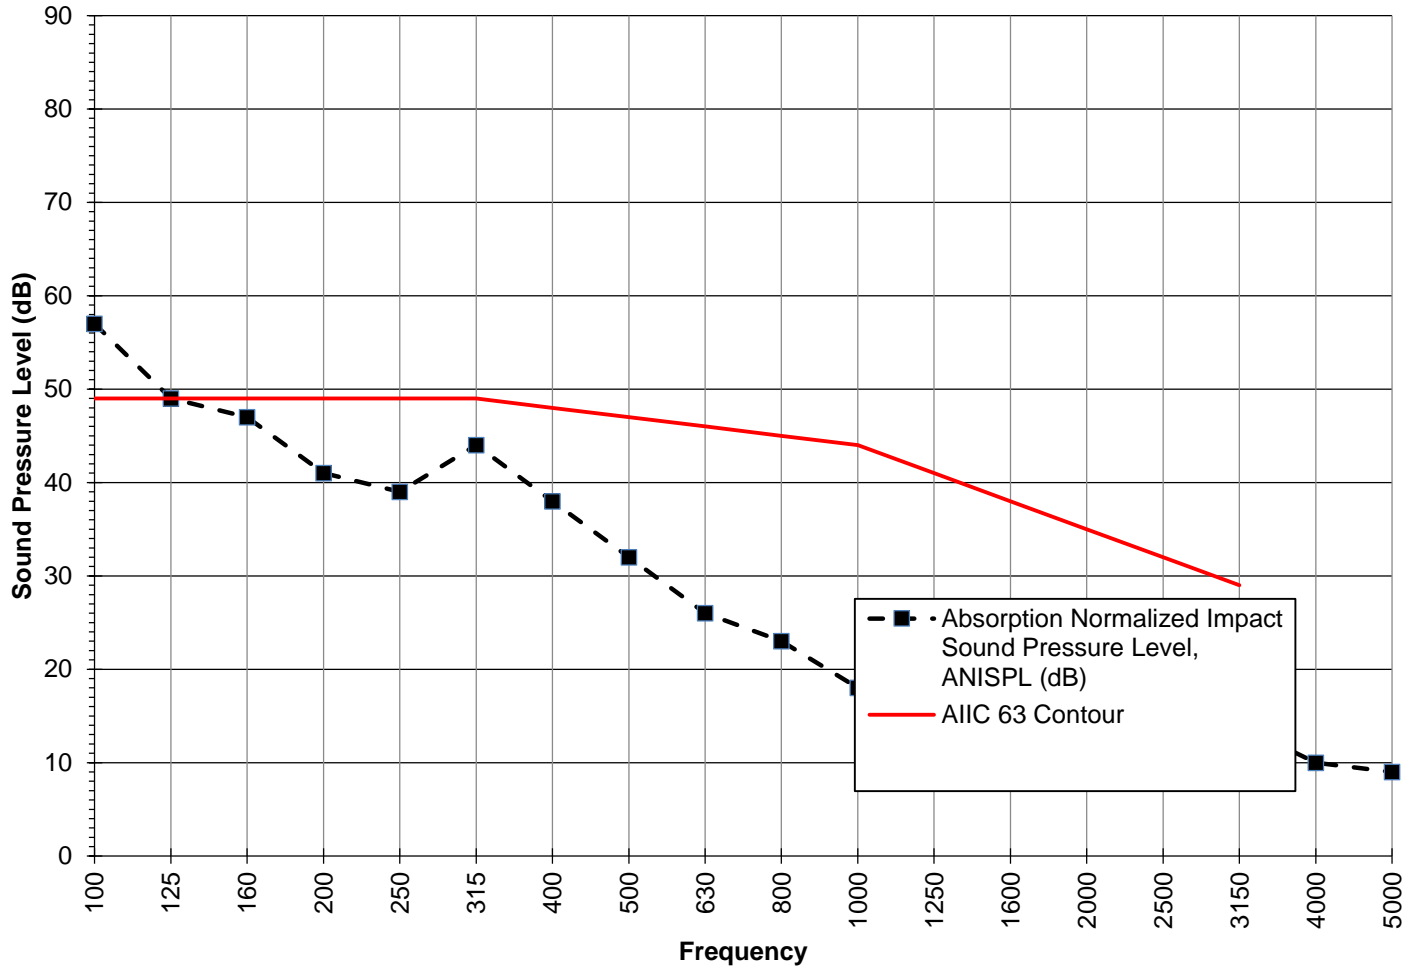

AIIC: 63

Test Conducted By:

Zane Wright, Project Consultant

Jake Pfitsch, Project Consultant
